FCPS New Secondary Facility (ies) Construction Schedule
Referendum First vs. Design First

ID	Task Name	Duration	Start	Finish
1	**Referendum First**	979 days	Tue 11/2/04	Fri 8/1/08
2	Referendum	1 day	Tue 11/2/04	Tue 11/2/04
3				
4	Hire Architect	56 days	Wed 11/3/04	Wed 1/19/05
5				
6	Design	272 days	Thu 1/20/05	Fri 2/3/06
7				
8	Bid/Hire Contrac	45 days	Mon 2/6/06	Fri 4/7/06
9				
10	Mobilization	30 days	Mon 4/10/06	Fri 5/19/06
11	VPSA Borrowing	1 day	Mon 10/2/06	Mon 10/2/06
12	VPSA Borrowing	1 day	Mon 10/1/07	Mon 10/1/07
13	Construction	575 days	Mon 5/22/06	Fri 8/1/08
14				
15				
16	**Design First**	1001 days	Wed 10/1/03	Wed 8/1/07
17	Hire Architect	56 days	Wed 10/1/03	Wed 12/17/03
18				
19	Design	272 days	Thu 12/18/03	Fri 12/31/04
20				
21	Public Hearings	45 days	Mon 1/3/05	Fri 3/4/05
22				
23	Referendum	1 day	Tue 4/5/05	Tue 4/5/05
24				
25	Bid/Hire Contrac	45 days	Wed 4/6/05	Tue 6/7/05
26				
27	Mobilzation	30 days	Wed 6/8/05	Tue 7/19/05
28	VPSA Borrowing	1 day	Mon 10/3/05	Mon 10/3/05
29	VPSA Borrowing	1 day	Mon 10/2/06	Mon 10/2/06
30	Construction	525 days	Thu 7/28/05	Wed 8/1/07

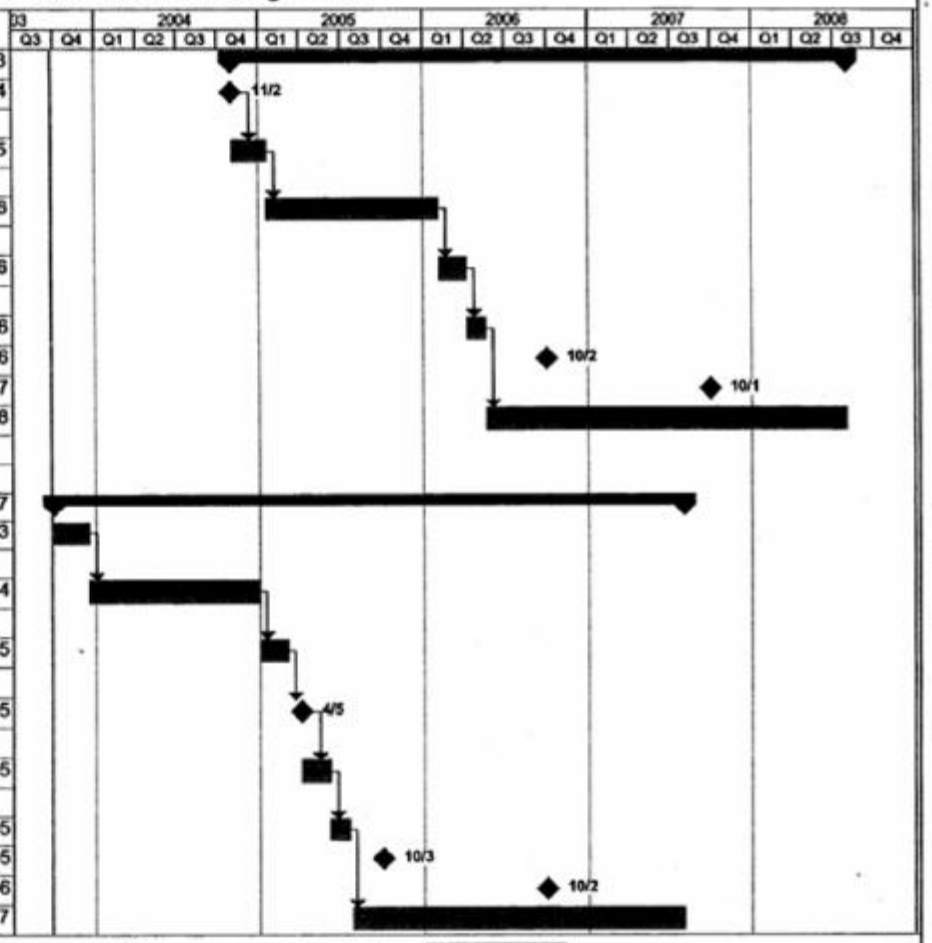

Project: NewHSProject2
Date: Wed 9/24/03

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
